South Mast Road Drainage Improvements

ID	Task Name	Duration	Start	Finish
1	**SOUTH MAST ROAD DRAINAGE IMPROVEMENTS**	**17 days**	**Fri 11/20/09**	**Wed 12/16/09**
2	**Lamson Ave**	**17 days**	**Fri 11/20/09**	**Wed 12/16/09**
3	Erosion Control	1 day	Fri 11/20/09	Fri 11/20/09
4	Site Meeting	1 day	Mon 11/23/09	Mon 11/23/09
5	Sewer Work	3 days	Tue 11/24/09	Mon 11/30/09
6	Porous Cross Section Sta 70+20 to 72+00	1 day	Tue 12/1/09	Tue 12/1/09
7	Drainage from Basin to DMH #12	1 day	Wed 12/2/09	Wed 12/2/09
8	Roadway 2' cut Sta 72+00 to 75+38	1 day	Thu 12/3/09	Thu 12/3/09
9	Porous Cross Section w/pipe Sta 72+00 to 75+38	5 days	Fri 12/4/09	Thu 12/10/09
10	Construct Basin	3 days	Fri 12/11/09	Tue 12/15/09
11	Restoration	1 day	Wed 12/16/09	Wed 12/16/09
12				
13	**West Union Drainage**	**14 days**	**Fri 11/20/09**	**Fri 12/11/09**
14	Erosion Control	1 day	Fri 11/20/09	Fri 11/20/09
15	Saw Cutting	1 day	Tue 11/24/09	Tue 11/24/09
16	Drain Pipe at outfall, MH 14, DMH 15 & CB #16	7 days	Mon 11/30/09	Tue 12/8/09
17	Prep for Pavement	2 days	Wed 12/9/09	Thu 12/10/09
18	Pave	1 day	Thu 12/10/09	Thu 12/10/09
19	Restoration	1 day	Fri 12/11/09	Fri 12/11/09

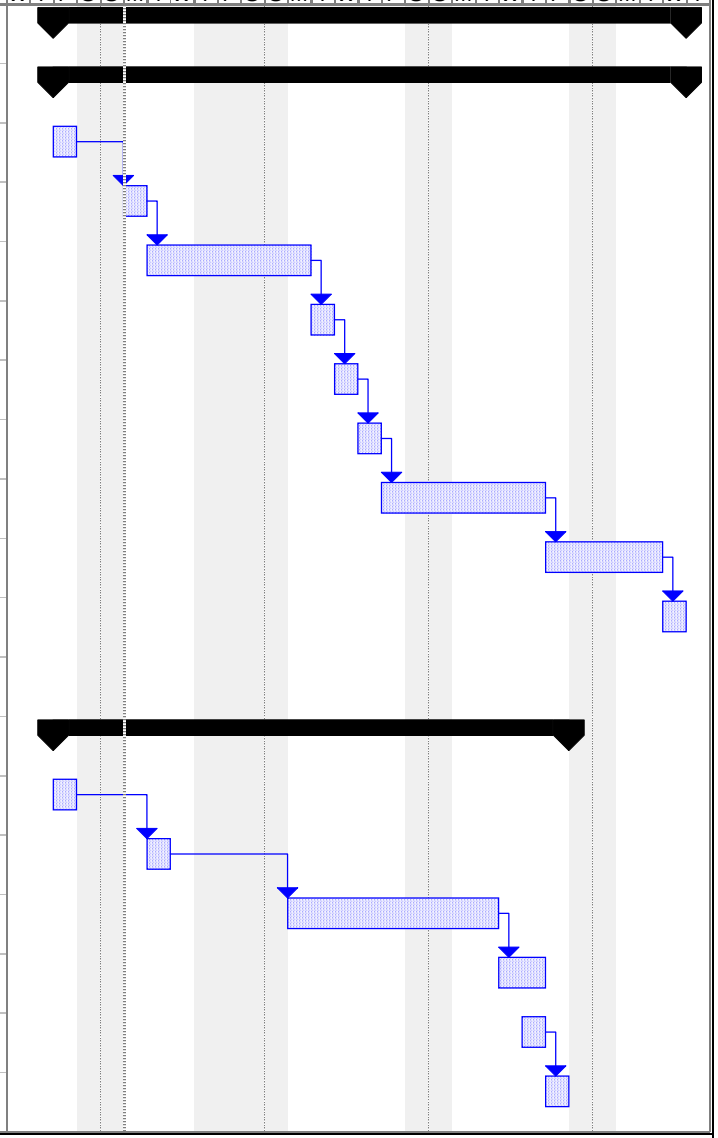

Project: 11.20.2009
Date: Mon 11/23/09
Deloury Construction Co. Inc

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline
